Appendix: CoreWeave Denton, TX (Core Scientific landlord) site status, as of Thu Oct 8, 2026, ~3:15 PM ET

Nebius Peer KPIs. Public sources only. Grade: Green (unchanged since Oct 5). Same layout and definitions as the Vineland appendix.

Definitions (team, as in capacity/vineland_site_appendix): Announced = company-stated build-out. Connected = power delivered into fully built, equipped halls (can sit idle until GPUs arrive); grid/utility MW is shown on its own row and is NOT IT MW. Active = power used by installed, operating IT. Billed = revenue-generating IT MW. Tags: R reported (company/regulator), P press/third party, D derived, E estimated, n/d not disclosed. [n] = sources.


1. Site facts

Item	Fact	Tag	Src
Owner / landlord	Core Scientific (Core Scientific Denton LLC); City of Denton ground lease to 12/31/2035, extends with the PPA	R	1
Tenant / operator	CoreWeave (colocation licence; CoreWeave pays utility costs); end customer n/d	R	1
Location / build	8171 Jim Christal Rd, Denton TX; ~64 ac (78.85 ac after 2024 amendment); 8 bldgs A–H, 370,284 sf; ex-bitcoin campus, HPC conversion from Q3'24; GC T5	R	1, 7

2. MW: announced / connected / active / billed

Stage	MW	Basis	Tag	Src
Announced	262 IT / 394 grid	full build	R	1, 2
Connected (grid / utility)	297 energized + 74 to energize	grid, not IT	R	3
Connected (halls)	~260	IT; 'substantially complete'	R	5
Active	~260 (250–262)	IT; landlord says billing	D	5
Billed	~260	IT; CORZ billing CoreWeave, mid-Jul	R	5
YE26 billed L / B / H	260 / 262 / 262	IT	E	6

Billed = landlord (CORZ) billing CoreWeave; CoreWeave's own billed MW at Denton n/d. Apr 21 8-K: Bldgs D–G ~132 MW billing, rest H2'26; Jul 28 deck: ~260 MW billing of >430 MW CORZ total [1, 5]. City (Sep 22) cites 391 MW electrical capacity [8].

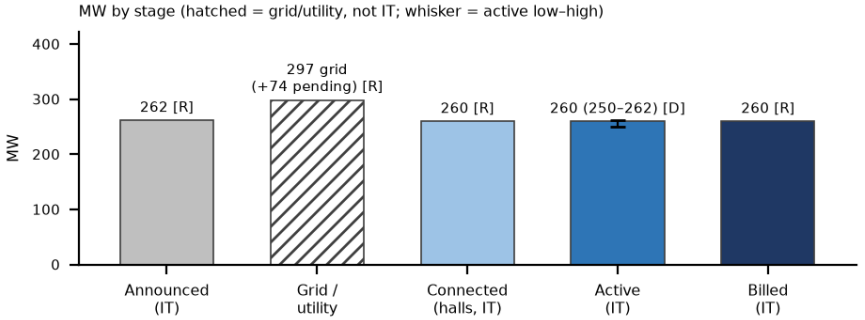

3. Power and interconnection

Item	Status	Tag	Src
Utility / ISO	Denton Municipal Electric PPA (~394 MW potential); ERCOT	R	2, 7
ERCOT status	297 MW 'Base Load, Pathway (a)' (energized before 3/25/2022), outside Batch Zero; +74 MW validated in ERCOT 2025 RTP, outside Batch Zero	R	3
Substations / grid	2 new on-site substations (CORZ-funded); DME/ERCOT upgrades by 2029; city: transmission near limits	R	7, 8
PPA headroom	DME (Sep 22): CORZ not yet at its PPA MW cap; no extra power requested; asked to lease more DME land 3–4 months earlier	R	8
On-site generation	Emergency / standby gensets only (PBR); campus is grid-powered	R	9

4. Permits (TCEQ / state / local)

Permit	Status / dates	Tag	Src
TCEQ PBR 179143	§106.511 standby engines/turbines, 'Core Scientific Data Center Site 1 And 2 Denton', ack 2025-02-11 (RN111355798)	R	9
Major NSR / PSD / Title V	None found: no Denton DC entry on TCEQ Title V list (data 10/8) or NSR list (run 10/8)	R absence	10
City	PPA + land-lease amendments approved 2024-11-19; no city tax incentives requested	R	7

5. Imagery, construction evidence and contract economics

Check	Finding	Tag	Src
Sentinel-2 Oct 5 v Sep 15	Fully roofed campus, no new pads; white-roof 17.6 v 18.7 ha (same metric; illumination noise). Not load evidence	D; read E	11
2023 → 2026 imagery	White-roof ~9.8 → ~18.7 ha; south pad from Oct-25; thermal confounded by mining-era load	D; E	6
Contract economics	CORZ–CoreWeave ~590 MW, '$10B+' over the term → ~$1.4M per MW-yr colocation (D, ~12 yrs). Facility rent, not compute $/MW. Denton $ n/d	R; D	5

What would change our view: (1) CORZ Q3 results ~Oct 23 [E] and CoreWeave Q3 ~early Nov [E]: confirm 262 MW complete/billing and a date for the +74 MW (bull: expansion past 262) [5, 12]. (2) Denton moratorium: 2nd hearing Oct 27, vote as early as Dec 1. City attorney: it 'does not necessarily stop an existing project', but CORZ's extra-land request could be caught (bear for expansion only) [8]. (3) ERCOT large-load audit reports Dec 10, PUCT Dec 17: reclassifying the +74 MW is the bear [3, 13]. Biggest risk: low for the 262 MW in service; only expansion optionality is exposed.

What changed since Oct 5: Since Oct 5: Denton moratorium process (Oct 27 hearing; vote ≥ Dec 1) and CORZ land request added; Oct 5 Sentinel-2 scene shows no change; MW unchanged.

Sources: [1] CORZ 8-K Ex.99.2 (2026-04-21) www.sec.gov/Archives/edgar/data/1839341/000119312526165121/d149019dex992.htm (acc. Oct 8) · [2] CORZ/CoreWeave PR (2025-02-26) www.businesswire.com/news/home/20250226866161/en/Core-Scientific-and-CoreWeave-Announce-%241.2-Billion-Expansion-at-Denton-TX-Site (acc. Oct 5) · [3] CORZ 8-K (2026-09-10, ERCOT status) investors.corescientific.com/sec-filings/all-sec-filings/content/0001839341-26-000023/0001839341-26-000023.pdf (acc. Oct 8) · [5] CORZ Q2'26 deck (2026-07-28) www.sec.gov/Archives/edgar/data/1839341/000183934126000013/q2fy26earningsdeck728am.htm (acc. Oct 5; sites/docs/corz_q226_deck.txt) · [6] Team: peers/sites/site_verification.md §1; sites.xlsx; strips/denton_tx_strip.png · [7] City of Denton (2024-11-20) www.cityofdenton.com/CivicAlerts.aspx?AID=922 (acc. Oct 5) · [8] Community Impact (2026-09-24) communityimpact.com/denton/government/denton-officials-weigh-data-center-moratorium-during-first-public-hearing/ (acc. Oct 8) · [9] TCEQ PBR 179143 records.tceq.texas.gov/cs/idcplg?IdcService=TCEQ_EXTERNAL_SEARCH_GET_FILE&Rendition=Web&dID=8656717 ; sites/docs/denton_tceq_pbr_179143.pdf (acc. Oct 5) · [10] TCEQ Title V pending (data 10/8/2026) www.tceq.texas.gov/assets/public/permitting/air/reports/applications/titlev-pending-permits.html ; NSR pending (run 10/8/2026) www.tceq.texas.gov/assets/public/permitting/air/reports/applications/nsr-pending-permits.html (acc. Oct 8) · [11] Sentinel-2 L2A S2B_14SPB_20261005 (Earth Search); sites/imagery/denton_tx/detail/denton_tx_2026-10-05_crop_oct8.png · [12] CORZ Q3 date (third party) www.marketbeat.com/earnings/reports/2026-10-23-core-scientific-inc-stock/ (acc. Oct 8) · [13] Gov. Abbott (2026-09-21) gov.texas.gov/news/post/governor-abbott-directs-tceq-to-halt-data-center-permits ; ERCOT audit timeline computelaw.blog/brief/texas-governor-pauses-environmental-permits-for-data-centers-until-state-audits-end/ (acc. Oct 8)

Appendix: IREN Childress, TX (Microsoft Horizons) site status, as of Thu Oct 8, 2026, ~3:15 PM ET

Nebius Peer KPIs. Public sources only. Grade: Green (H1–2) / Yellow (H3–4 by Q4'26), unchanged since Oct 5. Site grid MW includes legacy bitcoin load.

Definitions (team, as in capacity/vineland_site_appendix): Announced = company-stated build-out. Connected = power delivered into fully built, equipped halls (can sit idle until GPUs arrive); grid/utility MW is shown on its own row and is NOT IT MW. Active = power used by installed, operating IT. Billed = revenue-generating IT MW. Tags: R reported (company/regulator), P press/third party, D derived, E estimated, n/d not disclosed. [n] = sources.


1. Site facts

Item	Fact	Tag	Src
Owner / operator	IREN (SPV Ie US Development Holdings 3 Inc.); IREN-owned 576 ac	R	1, 2
Tenants	Microsoft: Horizons 1–4, 4 × 50 MW IT liquid-cooled GB300 NVL72, $9.7B / 5 yrs. NVIDIA: $3.4B in ~60 MW of existing halls from early 2027	R	3, 4
Location / legacy	620 FM 1033, Childress County TX; Phases 1–5 = 650 MW bitcoin 'operating data centers' (Aug-25), winding down	R	2, 5

2. MW: announced / connected / active / billed

Stage	MW	Basis	Tag	Src
Announced	750 grid; 200 IT (H1–4) + ~60 (NVIDIA)	H5–6 (2027) MW n/d	R	3, 4, 6
Connected (grid / utility)	750	grid incl. mining load	R	6
Connected (halls)	~100 (H1 + H2 commissioning)	IT	D	3
Active	75 (50–100)	IT, AI only	D	3, 7
Billed	50 (H1 accepted Aug 13)	IT; H2 n/d until acceptance	D on R	7
YE26 billed L / B / H	100 / 150 / 200	IT	E	8

Site grid load ≠ AI IT: the 750 MW interconnection still carries mining load. H2 'commissioning underway' and H3–4 'late-stage construction, targeting delivery in Q4 2026' (Aug 27) [3]; no H2 acceptance found as of Oct 8.

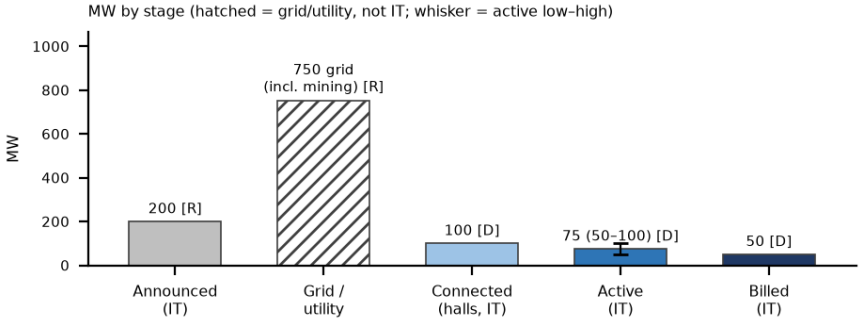

3. Power and interconnection

Item	Status	Tag	Src
Utility / ISO	AEP Texas / ERCOT; IREN-owned substations, dual diverse connection	R	2
ERCOT status	Existing energized load (raised 600 → 750 MW on 2024-07-24 after ERCOT study); not a Batch Zero new-interconnect case; 2nd bulk transformer energized for H1–2	R	5, 6
Regional grid	ERCOT-endorsed AEP Childress Area Transmission Improvement (Tier 2, ~$77.3M, ISD Nov 2031, CCN needed): area reliability, not site supply	R	9
On-site generation	None found; Title V filing implies permitted emission units (unit list n/d)	R abs.; E	10

4. Permits (TCEQ / state / local)

Permit	Status / dates	Tag	Src
TCEQ Title V #4951	'Childress Data Center', Ie US Development Holdings 3; received 2026-08-17; Administrative Complete (list data 10/8, unchanged since Oct 5)	R	10
Major NSR / PSD	None found (NSR pending list run 10/8: no IREN / Childress DC entry)	R absence	11
Sep 21 state pause	TCEQ issues no data-center permits until the ERCOT audit; Childress is on third-party lists of pending DC applications, so #4951 waits; operations continue meanwhile [E]	R; P; E	12
County	Ch. 312 abatements / Iris Reinvestment Zone (IE US entities)	R	13

5. Imagery, construction evidence and contract economics

Check	Finding	Tag	Src
Sentinel-2 Oct 5 v Sep 28	Mining sheds + new west/north halls + grey SE facility; white-roof 9.0 v 12.8 ha (same metric; sun/view noise, no demolition seen). H2–H4 not separable at 10 m	D; read E	14
2023 → 2026 imagery	White-roof 0.5 → 19–25 ha (Mar–Jul 26); thermal dominated by mining	D; E	8
Contract economics	Microsoft $9.7B / 5 yrs / 200 IT MW = $9.7M per IT MW-yr (bottom of the $9.7–16.7M comp band). NVIDIA $3.4B / 5 / ~60 = ~$11.3M (MW unlabeled). IREN: 'active discussions at ~$25M per MW (IT)', not signed	R; D	3, 15

What would change our view: (1) Horizon 2 acceptance PR and H3–4 delivery in Q4'26: each accepted 50 MW adds billed MW; a slip past Dec 31 leaves YE26 at the 100 MW low [3, 7]. (2) IREN Q1 FY27 results ~early–mid Nov [E]: H2–H4 status and NVIDIA 60 MW ramp [3]. (3) TCEQ compliance report Oct 19; ERCOT audit Dec 10 / PUCT Dec 17: #4951 stays unissued under the pause; bear only if the state moves against operating sites [12]. Biggest trigger: H2–H4 acceptance timing (YE26 billed 100 / 150 / 200).

What changed since Oct 5: Since Oct 5: no IREN 8-K; #4951 still Administrative Complete (TCEQ data 10/8) and now explicitly inside the Sep 21 permit pause; H2 still not accepted; Oct 5 Sentinel-2 adds nothing.

Sources: [1] Texas Comptroller data-center list (LD926028) comptroller.texas.gov/taxes/data-centers/data-center-lists.php (acc. Oct 5) · [2] IREN Childress page iren.com/data-centers/childress (acc. Oct 5) · [3] IREN FY26 results (2026-08-27) www.sec.gov/Archives/edgar/data/1878848/000187884826000051/irenreportsfy26results.htm (acc. Oct 8; sites/docs/iren_fy26.txt) · [4] IREN Q3 FY26 (2026-05-07, NVIDIA $3.4B) via peers/iren/iren_kpis.md · [5] IREN Aug-2025 update iren.gcs-web.com/static-files/ec8ec2a6-a1d1-4bb6-9cb9-bc2d436b9db9 (acc. Oct 5) · [6] IREN PR (2024-07-24) www.nasdaq.com/press-release/iren-increases-childress-power-capacity-600mw-750mw-2024-07-24 (acc. Oct 5) · [7] IREN 8-K Ex.99.1 (2026-08-13, H1 accepted) www.sec.gov/Archives/edgar/data/1878848/000114036126032638/ef20080141_ex99-1.htm (acc. Oct 8) · [8] Team: peers/sites/site_verification.md §2; sites.xlsx; strips/childress_tx_strip.png · [9] PUC Docket 55999 Item 173 interchange.puc.texas.gov/Documents/55999_173_1556587.PDF (acc. Oct 5) · [10] TCEQ Title V pending (data 10/8/2026) www.tceq.texas.gov/assets/public/permitting/air/reports/applications/titlev-pending-permits.html (acc. Oct 8) · [11] TCEQ NSR pending (run 10/8/2026) www.tceq.texas.gov/assets/public/permitting/air/reports/applications/nsr-pending-permits.html (acc. Oct 8) · [12] Gov. Abbott (2026-09-21) gov.texas.gov/news/post/governor-abbott-directs-tceq-to-halt-data-center-permits ; computelaw.blog/brief/texas-governor-pauses-environmental-permits-for-data-centers-until-state-audits-end/ (acc. Oct 8) · [13] Childress County tax abatements www.childresstx.us/pages/tax-abatements ; sites/docs/childress_county_abatement_notice_2023-08.pdf (acc. Oct 5) · [14] Sentinel-2 L2A S2A_14SLD_20261005 (Earth Search); sites/imagery/childress_tx/detail/childress_tx_2026-10-05_crop_oct8.png · [15] peers/comparison.xlsx Contracts_$MWyr rows P1 / NEW1 (comp band $9.7–16.7M)

Appendix: Crusoe Abilene, TX (Stargate; Oracle / OpenAI tenant) site status, as of Thu Oct 8, 2026, ~3:15 PM ET

Nebius Peer KPIs. Public sources only. Grade: Green (B1–6 delivered) / Yellow (B7–8 by YE26; expansion permit frozen). Oracle's Abilene MW is counted here only, not under Oracle.

Definitions (team, as in capacity/vineland_site_appendix): Announced = company-stated build-out. Connected = power delivered into fully built, equipped halls (can sit idle until GPUs arrive); grid/utility MW is shown on its own row and is NOT IT MW. Active = power used by installed, operating IT. Billed = revenue-generating IT MW. Tags: R reported (company/regulator), P press/third party, D derived, E estimated, n/d not disclosed. [n] = sources.


1. Site facts

Item	Fact	Tag	Src
Land / developer	Lancium (Clean Campus land, substations); Crusoe developer/builder via financing JV (Blue Owl per team files)	R; P	1, 14
Tenant / end user	Oracle (OCI) leases all 8 buildings; OpenAI is the end user (Stargate); NVIDIA GB200 NVL72	R	1, 2
Location	Longhorn Data Center, 615 FM 2404, Abilene, Taylor County (32.508, −99.777). Adjacent Crusoe–Microsoft 900 MW campus (2 × 336 IT, 2027+) excluded	R	7, 14

2. MW: announced / connected / active / billed

Stage	MW	Basis	Tag	Src
Announced	1.2 GW gross / 8 bldgs; ~824 IT implied	618 ÷ 0.75; Epoch ~843 IT	R; D; P	1, 2, 3
Connected (grid / utility)	200 (138 kV) + 1,000 (345 kV) subs; ~360 on-site gas	grid / on-site, not IT	R	4, 5
Connected (halls)	618 delivered (6 of 8 bldgs, 75%)	basis unstated; read as IT	R; basis E	2
Active	618 (421–618)	IT; delivered + accepted (R) read as active; low = Epoch to Jul-27	D on R; P	2, 3
Billed	~618 (Oracle → OpenAI)	acceptance 'only 24 hours'	D	2
YE26 billed L / B / H	618 / 721 / 824	IT; B7–8 ≈ 103 each	E	2, 3

CHANGED vs Oct 5 (active 200 / 421 / 421): Oracle's Sep 10 call (FQ1 FY27) says 6 of 8 buildings, 618 MW and 75% of capacity are delivered to the customer, with 131k GPUs delivered there in the quarter [2]. The JV's lease billing to Oracle is n/d.

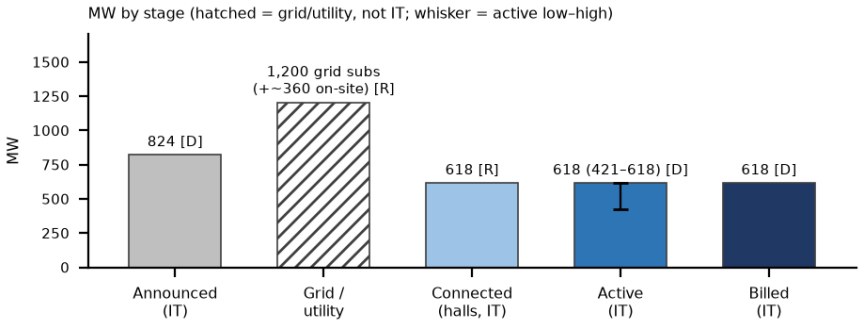

3. Power and interconnection

Item	Status	Tag	Src
Utility / ISO	ERCOT; AEP interconnection via Lancium 138 kV and 345 kV substations	R	4
345 kV substation	1st transformer 2025-12-19; all 5 MPTs by 2026-03-10 (3 temporary); permanent swaps targeted Oct 2026	R	4
On-site generation	Std Permit 177263: 5 Solar Titan 350 + 5 GE LM2500 ≈ 360.5 MW, 8,760 h/yr, on-site use only; ~62 diesel gensets (PBR, reported 177262). Crusoe: turbines are backup	R; P	5, 6

4. Permits (TCEQ / state / local)

Permit	Status / dates	Tag	Src
177263 (issued)	Abilene DC 1 LLC dba Crusoe; modification reviewed Jan 2025	R	5
182126 / PSDTX1688 / GHGPSDTX263	Crusoe Energy Systems, Longhorn DC (RN112029061): filed 2025-11-07; NORI 11-19; NAPD + draft 2026-08-05; TCEQ list: 'Technically Complete' (data 8/28, run 10/8). NOT issued	R	7, 8
Scope of 182126	Bldgs 9–10 / added on-site generation: 39 simple-cycle turbines, up to ~1,330 MW (EIP) vs 41 turbines + 18 gensets (Tribune)	R; P	7, 9, 6
Sep 21 state pause	No TCEQ data-center permits until ERCOT audit; TCEQ compliance report due Oct 19; ERCOT audit reports Dec 10, PUCT Dec 17	R; P	10, 11
Incentives	City 85% / Taylor County 80% 10-yr abatements, one agreement per building	P	12

5. Imagery, construction evidence and contract economics

Check	Finding	Tag	Src
Sentinel-2 Oct 5 v Sep 15	All 8 halls roofed with chiller yards; large new works on the southern (Microsoft) campus. Beige roofs read low on the white-roof metric (14.9 v 10.9 ha); energized halls not visible at 10 m	D; read E	13
Thermal	Landsat Jun–Aug anomaly +0.40 → −0.41 °C: not informative (red soil)	E	14
Contract economics	Oracle–OpenAI ~$300B / 5 yrs (WSJ; not in Oracle filings) = $13.3M per stated MW-yr, $16.0M per IT MW-yr if 4.5 GW is gross: inside the $9.7–16.7M band. Site lease n/d. JV shell + power ≈ $12.5M per gross MW	P; D	15, 16

What would change our view: (1) TCEQ report to the Governor Oct 19: as written the pause freezes 182126 (Bldgs 9–10, ~1.3 GW gas) only; extension to modifications or turbine operation would hit B1–8 backup (bear) [10, 11]. (2) Permanent 345 kV transformer swaps 'by Oct 2026' and Oracle FQ2 FY27 (~mid-Dec, E): 8 of 8 delivered (~824) is the bull; Epoch projected 843 IT ~Nov 1 [3, 4]. (3) ERCOT audit Dec 10 / PUCT Dec 17; Legislature from Jan 2027 on incentives [11]. Biggest risk: growth past 8 buildings is frozen until the audit; the 618 MW in service is not.

What changed since Oct 5: Since Oct 5: active base 421 → 618 MW on Oracle's Sep 10 statement (in the Oracle pack, not previously in the site view); 182126 confirmed not issued (Technically Complete); EIP turbine count; ERCOT Dec 10/17 dates.

Sources: [1] Crusoe PR (2025-09-30) www.crusoe.ai/resources/newsroom/crusoe-announces-flagship-abilene-data-center-is-live (acc. Oct 8); 1.2 GW / 8 bldgs per Crusoe JV PR 2025-05-21 (sites.xlsx) · [2] Oracle FQ1 FY27 call (2026-09-10; transcript 09-11) www.fool.com/earnings/call-transcripts/2026/09/11/oracle-orcl-q1-2027-earnings-call-transcript/ (acc. Oct 8) · [3] Epoch AI epoch.ai/data/ai-data-centers/directory/openai-stargate-abilene (acc. Oct 5) · [4] Mortenson www.mortenson.com/projects/abilene-data-center-development (acc. Oct 5) · [5] TCEQ Std Permit 177263 tech review: sites/docs/abilene_tceq_177263_tech_review.pdf · [6] Texas Tribune / Floodlight (2026-07-09) www.texastribune.org/2026/07/09/texas-data-centers-ai-power-plants-pollution-state-permits/ (acc. Oct 5) · [7] TCEQ 182126 plain-language summary www.tceq.texas.gov/downloads/permitting/air/bilingual/pending-permit-notices/182126-pls-english.pdf ; sites/docs/abilene_tceq_182126_napd.pdf, _nori.pdf (acc. Oct 8) · [8] TCEQ NSR pending (run 10/8/2026) www.tceq.texas.gov/assets/public/permitting/air/reports/applications/nsr-pending-permits.html (acc. Oct 8) · [9] EIP Oil & Gas Watch oilandgaswatch.org/alert/fc44e871-e7e9-4d4e-af22-bce4133e16d3 (acc. Oct 8) · [10] Gov. Abbott (2026-09-21) gov.texas.gov/news/post/governor-abbott-directs-tceq-to-halt-data-center-permits (acc. Oct 8) · [11] Texas Lawbook texaslawbook.net/abbott-orders-statewide-pause-on-texas-data-center-permits/ ; computelaw.blog/brief/texas-governor-pauses-environmental-permits-for-data-centers-until-state-audits-end/ (acc. Oct 8) · [12] DCOA (2025-05-01) developabilene.com/2025/05/01/project-radiance-powering-the-future-of-ai-in-abilene-texas/ (acc. Oct 5) · [13] Sentinel-2 L2A S2A_14SMA_20261005 (Earth Search); sites/imagery/abilene_tx/detail/abilene_tx_2026-10-05_crop_oct8.png · [14] Team: peers/sites/site_verification.md §4; sites.xlsx; strips/abilene_tx_strip.png; thermal/abilene_tx_landsat_st.csv; peers/oracle/oracle_kpis.xlsx Inputs Q40 (Blue Owl) · [15] peers/comparison.xlsx Contracts_$MWyr O2 (WSJ) / NEW8 · [16] peers/private/private_peers.md (Crusoe K14, D)

Appendix: Oracle (OCI) Port Washington, WI (Vantage 'Lighthouse'; Stargate) site status, as of Thu Oct 8, 2026, ~3:15 PM ET

Why this site: Oracle's largest live AI site is Abilene, the SAME campus as Crusoe Abilene (Oracle is the tenant), so it is counted once, under Crusoe. Port Washington is Oracle's separable key site. Shackelford County TX (Oracle: 'our next gigawatt scale campus', not delivered in FQ1) not built: thinner public record (gap). Grade: Yellow/Red vs end-2027 handover (unchanged).

Definitions (team, as in capacity/vineland_site_appendix): Announced = company-stated build-out. Connected = power delivered into fully built, equipped halls (can sit idle until GPUs arrive); grid/utility MW is shown on its own row and is NOT IT MW. Active = power used by installed, operating IT. Billed = revenue-generating IT MW. Tags: R reported (company/regulator), P press/third party, D derived, E estimated, n/d not disclosed. [n] = sources.


1. Site facts

Item	Fact	Tag	Src
Developer / owner	Vantage Data Centers (Wisco Acquisition Co.); $15B; 4 bldgs, ~2.5M sf	R; P	1, 2
Tenant / end user	Oracle (OCI) for OpenAI (Stargate); turnover in phases from end-2027	P	2
Location	North Port Washington, Ozaukee County WI; 672 ac (later phases up to 3.5 GW, press)	P	1, 3

2. MW: announced / connected / active / billed

Stage	MW	Basis	Tag	Src
Announced	~902 IT / 1.3 GW electrical	Vantage IT v utility total	R; P	1, 4
Connected (grid / utility)	0	~310 requested for 2027; 438 peak 2027	P	4
Connected (halls)	0	20–25% complete; 2 of 4 halls enclosed	R; P	2, 5
Active	0	IT	R	6
Billed	0	IT	R	6
YE26 / YE27 L / B / H	0 / 0 / 0; YE27 0 / ~310 / 438	YE27 = grid MW	E	4, 5

Oracle (Sep 10): 'neither Shackleford nor New Mexico or Wisconsin or Michigan were delivered in Q1' [6]. Utility filings (via press) show Vantage asked ATC for ~310 MW in 2027 and 1.3 GW from 2028 [4].

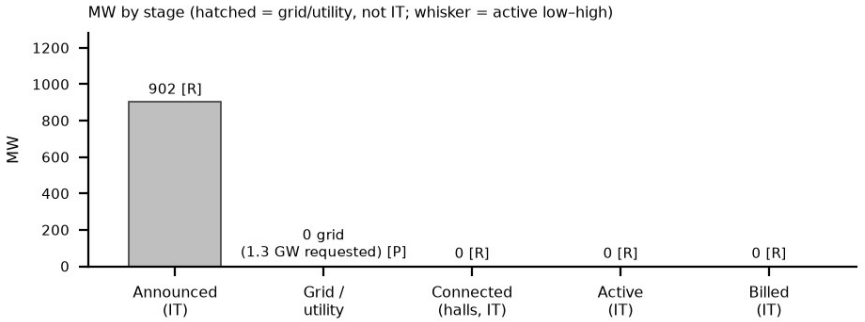

3. Power and interconnection

Item	Status	Tag	Src
Utility	We Energies (very-large-customer tariff; PSC 6630-TE-113 collateral rules; Oracle dropped its court challenge Aug 17)	R; P	3, 7
Transmission	ATC Ozaukee County project $1.39–1.67B, new Decker substation; construction Dec 2026 – Dec 2027	R	8
PSC status	Completeness revoked Aug 2026; case closed Sep 10; ATC refiled (Sep 14 per Wisconsin Watch, Sep 18 per TechRadar); completeness decision expected ~Oct 19	P	4, 5, 9
Aterio timing	Partial power Oct 2027 earliest / Dec 2027 base / Jun 2028 extended; full 1.3 GW Aug 2028 / Oct 2028 / Apr 2029	P	5
On-site generation	Up to 45 emergency diesel engines, 87 MW: backup only	R	10

4. Permits (TCEQ / state / local)

Permit	Status / dates	Tag	Src
WDNR air	Construction 25-MIN-094 + operation 24618528A-F01, final 2026-06-12	R	10
PSC (ATC line)	Refiled; completeness pending (~Oct 19)	R; P	8, 9
City	TIF $458.6M	P	1

5. Imagery, construction evidence and contract economics

Check	Finding	Tag	Src
Sentinel-2 Oct 6 v Sep 11	More roofs closed: white-roof 28.9 v 22.9 ha (+6 ha, same metric); still a construction site; no energized power plant visible at 10 m	D; read E	11
Press photos	Ozaukee Press aerial 2026-09-21: first 555k sf building enclosed; Sep 18 tour; 2,800–3,000 workers/day	P	2
Contract economics	Oracle–OpenAI ~$300B (WSJ) program-level, $13.3–16.0M per MW-yr; site lease n/d	P; D	12

What would change our view: (1) PSC completeness decision ~Oct 19 (with ATC's MISO voltage-device filing): a clean finding keeps Aterio's base (partial power ~Dec 2027); another rejection moves to the extended case (Jun 2028) [5]. (2) Oracle FQ2 FY27 (~mid-Dec, E): any change to 'H2 2027' Wisconsin delivery [6]. (3) Watch for a temporary / bypass supply for the ~310 MW 2027 request; Vantage says portions go live while the rest is built [2, 4]. Biggest risk: grid, not construction: halls can be ready before power (connected 0 into late 2027).

What changed since Oct 5: Since Oct 5: PSC completeness ~Oct 19 trigger, ATC refile-date conflict and the ~310 MW 2027 request added; Oracle confirms no Wisconsin delivery in FQ1; Oct 6 Sentinel-2 +6 ha roof.

Sources: [1] Ozaukee Press (2025-10-22) www.ozaukeepress.com/content/openai-oracle-run-stargate-port-data-center (acc. Oct 5) · [2] Ozaukee Press (2026-09-23) www.ozaukeepress.com/content/data-center-size-%E2%80%98-insane%E2%80%99 (acc. Oct 8) · [3] Data Center Census datacentercensus.com/dc/port-washington-lighthouse-wi (acc. Oct 8) · [4] TechRadar (2026-10-04) www.techradar.com/pro/a-meaningful-risk-oracles-massive-1-3-gw-wisconsin-ai-campus-faces-severe-power-delays-as-grid-review-restarts-pushing-customer-delivery-past-2027 (acc. Oct 8) · [5] Aterio (BusinessWire 2026-09-30) www.streetinsider.com/Business+Wire/Aterio+Flags+Delay+Risk+for+Oracle%E2%80%99s+1.3+GW+Wisconsin+Data+Center/27125698.html ; constructionreviewonline.com/project-lighthouse-delays-threaten-oracles-2027-wisconsin-data-center-launch/ (acc. Oct 8) · [6] Oracle FQ1 FY27 call (2026-09-10) www.fool.com/earnings/call-transcripts/2026/09/11/oracle-orcl-q1-2027-earnings-call-transcript/ (acc. Oct 8) · [7] PSC doc 593736 apps.psc.wi.gov/ERF/ERFview/viewdoc.aspx?docid=593736 (acc. Oct 5) · [8] PSC doc 597276 apps.psc.wi.gov/ERF/ERFview/viewdoc.aspx?docid=597276 (acc. Oct 5) · [9] Wisconsin Watch wisconsinwatch.org/2026/09/wisconsin-port-washington-data-center-atc-restarts-push-grid-upgrades-transmission-utility/ (acc. Oct 5) · [10] WDNR 25-MIN-094 final www.wpr.org/wp-content/uploads/2026/07/dnr.state_.wi_.us_Apps_AM_WARP_Documents_PROD_Final_63297.pdf ; sites/docs/wi_dnr_vantage_25-MIN-094_final.pdf (acc. Oct 5) · [11] Sentinel-2 L2A S2B_16TDP_20261006 (Earth Search); sites/imagery/portwash_wi/detail/portwash_wi_2026-10-06_crop_oct8.png · [12] peers/comparison.xlsx Contracts_$MWyr O2; team peers/sites/site_verification.md §6; sites.xlsx
